Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

03/28/23

513 12 Street Owners Group 513 12th Street Brooklyn, NY 11215

Rimkus New York PLLC. 77 Water Street Suite 836 New York, NY 10005 Tel: 866-299-3370


> 513 12th Street, Brooklyn, NY 11215 Facade Repairs Mobilization work in progress



DOB work permit and TPP posted on the front door

Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Approved DOB Drawings

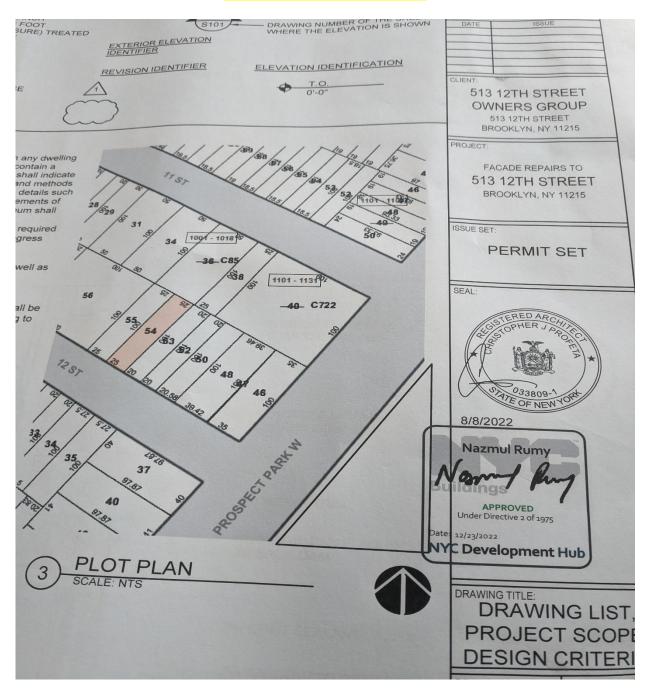

Office 718-369-1001 Fax 718-369-7059


Approved CD5


			File Representative—Last Name Andrade Lopez Forde Febo	
ui	Idings .	C	CD5: Suspended Scaffold Application File 3 copies / Application must be typewritten	
-	Application Type			
	x Initial ☐ Amendment ☐ Renewal ☐ This Is	an Indi	dustrial Roped Access Job This is a Site Safety Job	
2	Location Information		6133 Lot 7501	
	Borough Brooklyn	ock (Number of Stories 8	
2	Address 513 12th Street			
3	Filling Representative Information	on #	3844 / 3953 / 8082 / 8065	
	Name Andrade / Lopez / Forde / Febo Registrat Business Name Rigging Consultants Inc.	OH 9F		
	Address 555 Longfellow Avenue	City E	Bronx State NY Zip 10474	
	Phone 718-292-0099 Fex E	Mail	manny@riggingconsultants.com	
4	Rigger/Sign Hanger Information			
	Name Ataf A. Nawaz Lice	nse#	6570	
	Business Name Commercial Bdg Rest.	City	Brooklyn State NY Zip 11215	
	Address 119 14th Street Phone 718-369-1001 Fax	-Mail		
5				
9	Name Gisela Starton	Title	VP	
	Business Name 513 12th Street Owners Corp	Market Market		
	Address 5 Brewster Street #179		Glen Cove State NY Zip 11542	
	Phone 646-483-7304 Fax	-Mail	Starton @513Owners.com	
6			Date Submitted Stamp	
	Description of Work to be Performed: Facade Restoration		Date Submitted Stamp	
	Tacade (Vestoration		The man was need to be the bottom to	
			Walter and V End	
			FEB 1 0 2023	
	The second secon			
			THE CITY OF NEW YORK DEPOSITION OF BUILDINGS	
			DIVISION OF BRANES AND DERRICKS	
	Expected Start Date: Upon Approv Approximate Duration of Job: 1 Year	16		
	7 Cintements and Clanatures			
	I certify that the aubject work and actup of aquipment will be done under my supervision or under the supervision of Ataf A. Nawaz (Supervisor, Foreman, or Rigger/Sign Hanger). The work will be done in a safe and workman-like manner. Faisification of any statement is a misdemensor and is punishable by a fine or imprisonment, or both. It is unlawful to give to a city employee, or for a city employee to accept, any benefit, monetary or otherwise, either as a gratuity for property performing the job or in exchange for special consideration. Violation is by uninhable by imprisonment or fine or both. I understand that if I am found after property performing the job or in exchange for special consideration. Violation is punishable by imprisonment or fine or both. I understand that if I am found after hearing to have knowingly or negligently made a false statement or to have knowingly or negligently faisified or allowed to be faisified any certificate, form, signed statement, application, report or certification of the correction of a violation required under the provisions of this code or of a rule of any agency, I may be barred from filing further epplications or documents with the Department.			
	Foreman, or Rigger/Sign Hanger). The work will be done in a safe and workman, like manner fine or imprisonment, or both. It is unlawful to give to a city employee, or for a city employee.	accepi	pt, any benefit, monetary or otherwise, either as a gratuity for isonment or fine or both. I understand that if I am found after	
	properly performing the job of in exchange to appear constraints in the performance of th	gently f	raisified or allowed to be falsified any certificate, form, signed slons of this code or of a rule of any agency, I may be barred from	
	filing further applications or documents with the Department.	od Dile	gger/Sign Hanger Date	
1	Name of Licensed Rigger/Sign Hanger (please print)	a Rigg	02/06/2023	
10	Ataf A. Nawaz	min		
	Internal Use Only		WHILE	
	Approved by Examiner:	2023	SR23/0308	
	1114(4) -1144			
	Signature of Examiner: DEPARTMENT OF NO. OF FRAMES.	BUHLD	Expiration Date:	
	O. CANDON - SPERION OF CRARES	ANG D	DERRICES 05/01/2-3	

Office 718-369-1001 Fax 718-369-7059

Staging area



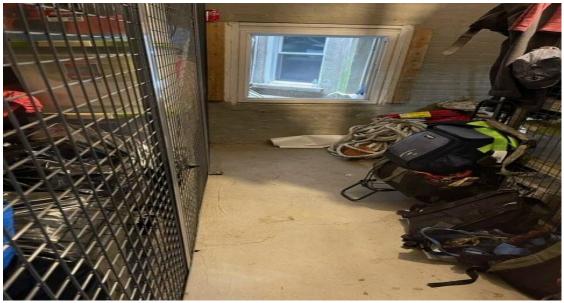

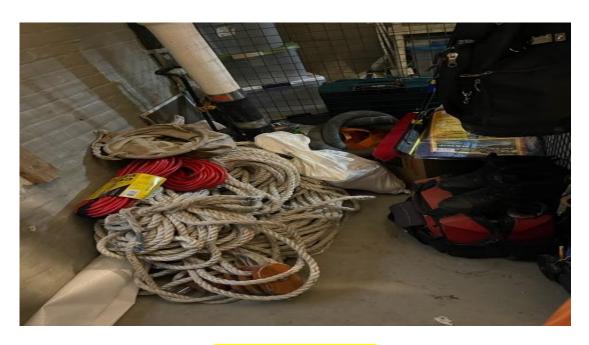



Material Hoist installed




Office 718-369-1001 Fax 718-369-7059

Outrigger installation work in progress

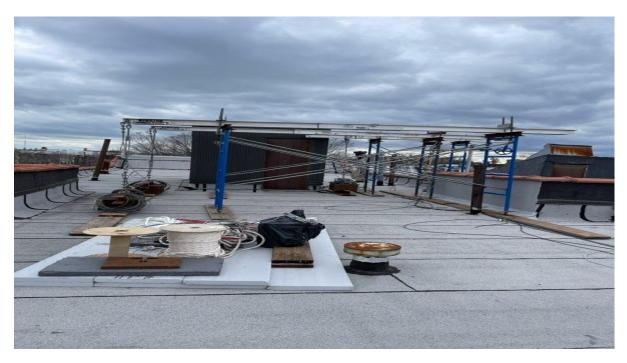

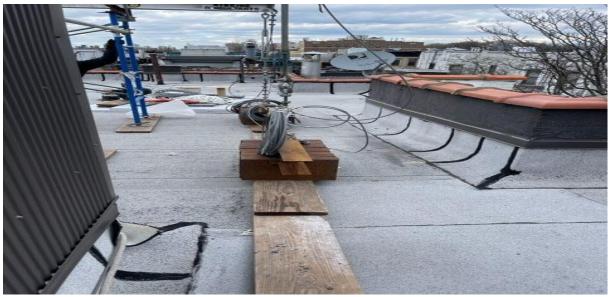

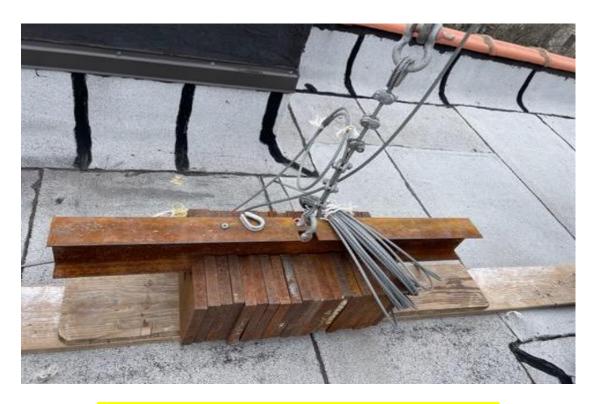


Anchor plates installed awaiting pull test Thursday 3/30/23



119 14th St, BROOKLYN NY 11215 (718) 369-1001 F (718) 369-7059

Office 718-369-1001 Fax 718-369-7059

Scaffold almost ready

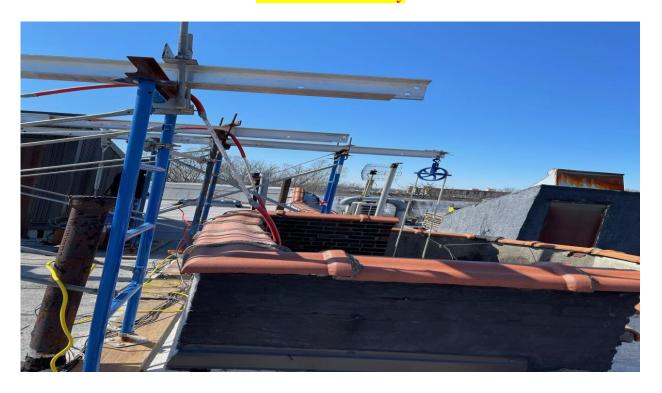



Office 718-369-1001 Fax 718-369-7059


Cutting work in progress






Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Pull test passed

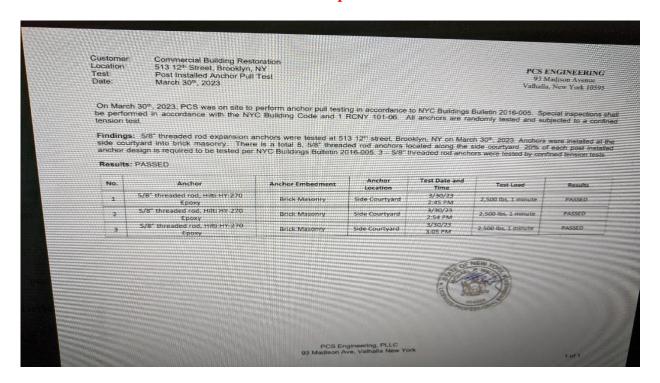

Electrical permit for panel box

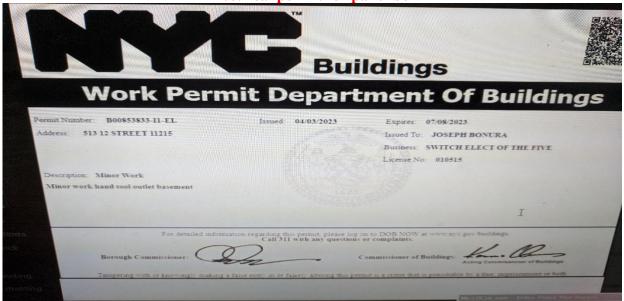

Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Approved bricks "Patriot & 53 DD STD" to be mixed

Profeta, Christopher

Fri, Mar 31, 1:25 PM (4 days ago)

to me, James, Richie, Mauricio

Hi all, sorry I've been in the field and traveling for the past few days. As far as the brick goes, are you able to mix the two as it seems to be that way on the existing wall.

Christopher Profeta Practice Leader

Electrical panel installed






Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Misc damaged brick removal and replacement. Contract total is 50



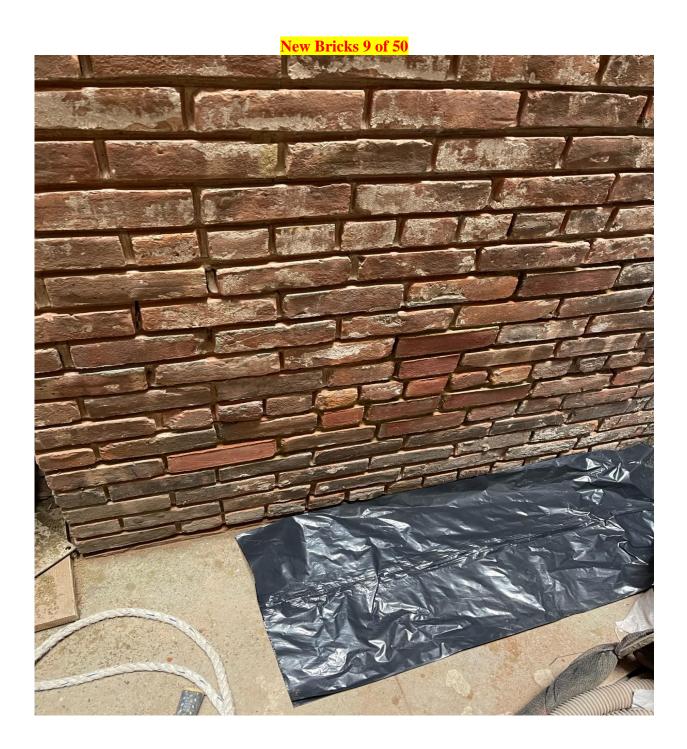

Office 718-369-1001 Fax 718-369-7059

Pointing work





Office 718-369-1001 Fax 718-369-7059



10 bricks removed & replaced – Total is 19 of 50









Office 718-369-1001 Fax 718-369-7059

Additional 31 Bricks removed and replaced. The total contract amount is 50. The total amount of bricks removed and replaced is 50.

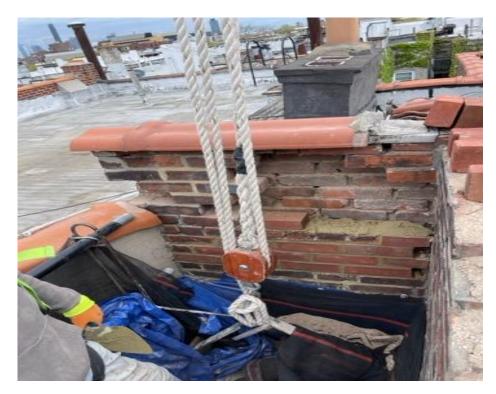



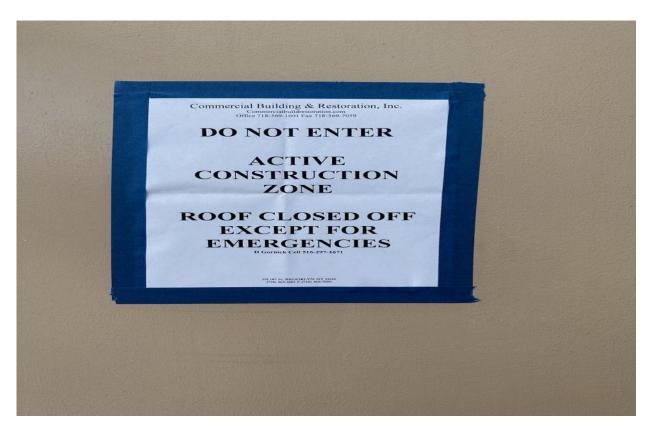



Office 718-369-1001 Fax 718-369-7059


Parapet wall work in progress






Office 718-369-1001 Fax 718-369-7059

Protection installed

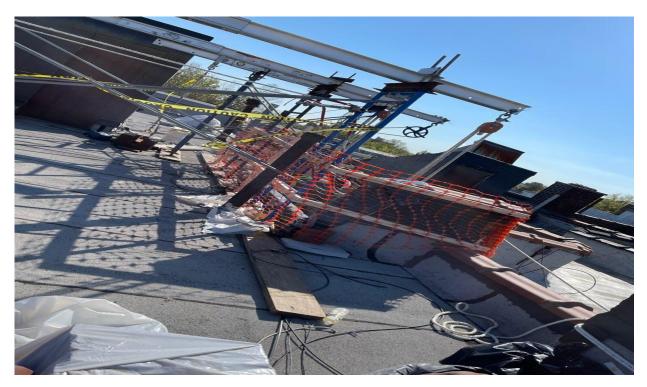

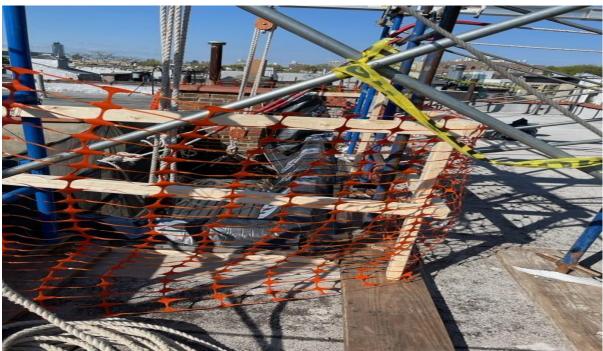


Office 718-369-1001 Fax 718-369-7059

Brick removal work in progress




Stucco work in progress

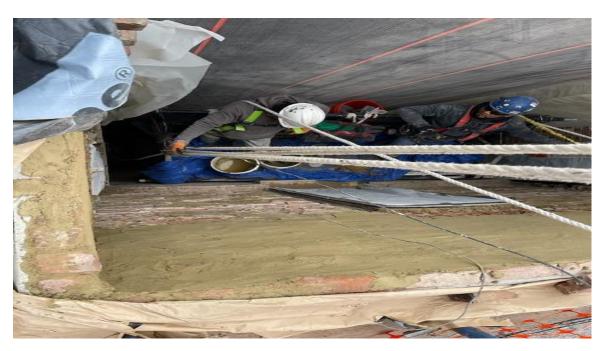





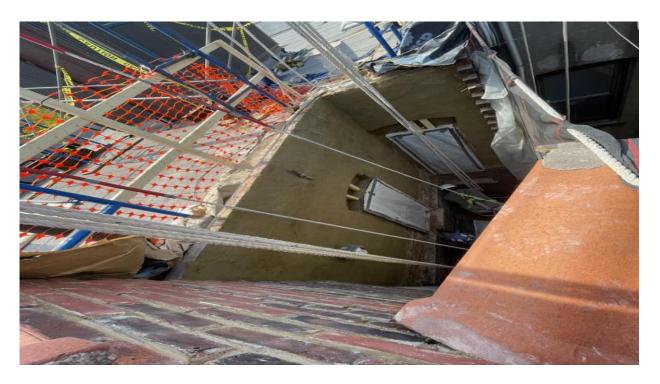





Office 718-369-1001 Fax 718-369-7059

Brickwork removed to the 4th floor window sill as per our contract



4th floor window sill

New approved brick work in progress









Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Brick ties specifications below

11:12 🖨 🗏 🖫 🖽	(☼ LTE⊿
← 12345SVSEISVA.	pdf 🗟 🚓 :
Seismic Anchors an 345-SV Seismic-Notch Veneer Ar	
	Δ Δ Δ
345 SV - SI VENEER A	SEISMIC-NOTCH ANCHOR
DRAWINGS FOR ILLUSTRATIVE PURPOSES ONLY The 345-SV Veneer Anchor features a Seismic Notch that Finish:	CONTINUOUS WIRE
accomodates 9 gauge or 3/16*Ø continuous wire while providing superior pull-out strength. Note: Hol	hmann & Barnard recommends Stainless Steel for iximum protection against corrosion.
Hot-Dip Galvanized after fabrication: ASTM A153/A153M-B (1.5 oz/ft²) Note: Hohmann & Barnard will certify to a minimum of 2.0 oz/ft² Wire (Stainless Stee): ASTM A580/A580M - AISI Type 304 or Type 316 Sheet Metal (Carbon Stee): ASTM A1088/A1088M Zinc Coating: Hot-Dip Galvanized: ASTM A153/A153M Class B (1.5 oz/ft²) (sheet metal ties and anchors galvanized after fabrication) Note: Hohmann & Barnard will certify to a minimum of 2.0 oz/ft²	auge
Sheet Metal (Stainless Steel): ASTM A666, ASTM A480/480M, and ASTM A240/A240M - AISI Type 304 or Type 316 H&B manufactures steel wire products from a minimum of 95% recycled material.	Dimensions: 345-SV is 11/2" wide x 16 ga., 14 ga., or 12 ga., allable in any length with 9/32"/2 hole
This desired a written content HOHMANN & BARNARD, Inc. Branch/Subsidiary Locations:	Since each construction project is unsue, the appropriate selection and use of any confidence of the project in particular that the project in question, and the project in question, and/or data sheet is the confidential and proprietary information of Hofmann & and/or data sheet is the confidential and proprietary information of Hofmann & or the project in question, and/or data sheet is the confidential and proprietary information of Hofmann & or the project in the pr
CORPORATE HEADQUIARTERS 30 Rasons Court Hauppauge, NY 11788 T: 800.645.0616 F: 631.234.0683 www.h-b.com ALABAMA - ARIZONA - ILLINOIS MARYLAND - NEW YORK PENISYLVANIA - TEXAS - UTAH CANADA	RESET FORM SAVE FORM SAVE FORM LOCK & HIDE BU
	B

Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Approved Mortar Documentation

Mon, Apr 3, 9:28 AM

to me, Chris, Richie, Mauricio

Hi Doug, The building is fine with your recommendation. Chris, please let us know if you have a different opinion. Thanks, James



Douglas Gornick < commercial building restoration @ gmail.com > Tue, Apr 4, 9:00 AM


to James, Chris, Richie, Mauricio, me

Since time is of the essence CBR will order the Specmix #407.


Thank you, Doug

Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

LPC approval for the Terracotta coping

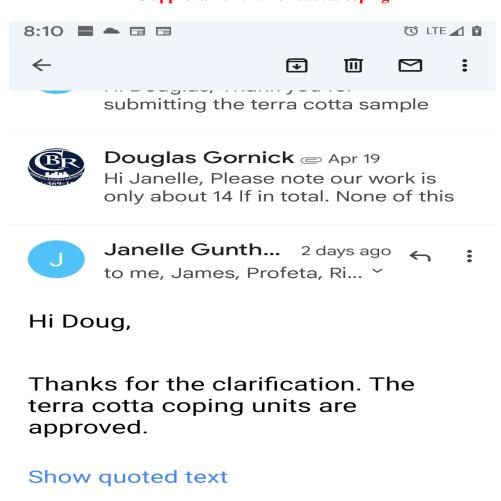



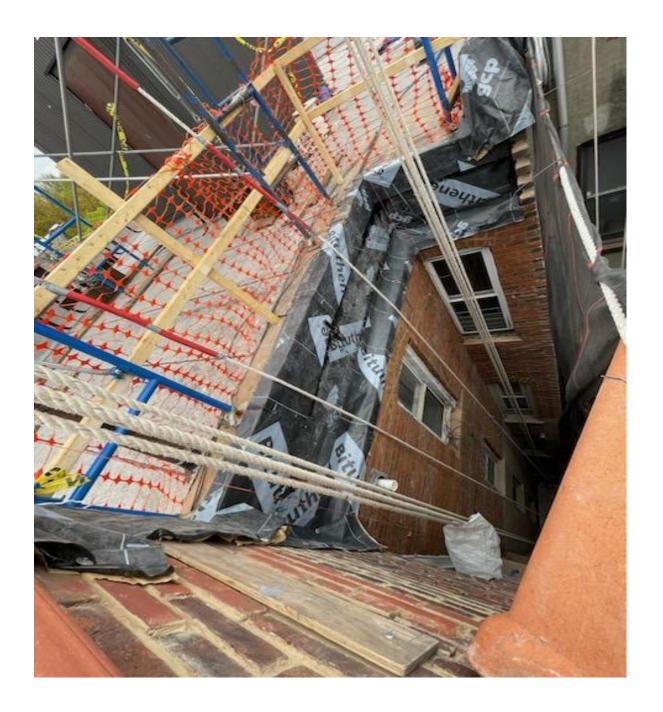

Office 718-369-1001 Fax 718-369-7059

Sill waterproofing installed



Sill reinstalled







Note - ALL window caulk work is completed

Commercialbuildrestoration.com Office 718-369-1001 Fax 718-369-7059

Parapet wall rebuilding work in progress




Level confirming straight wall









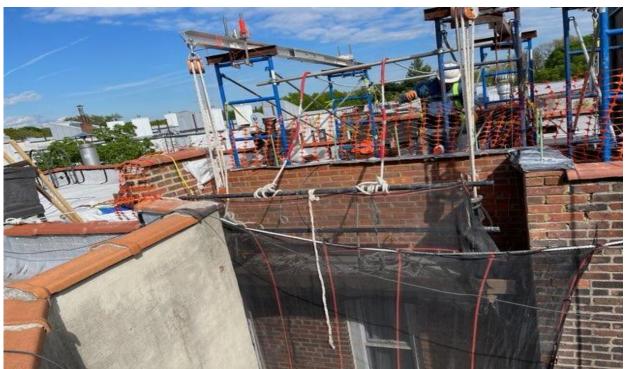













Office 718-369-1001 Fax 718-369-7059


Approved LPC camelback copings installed









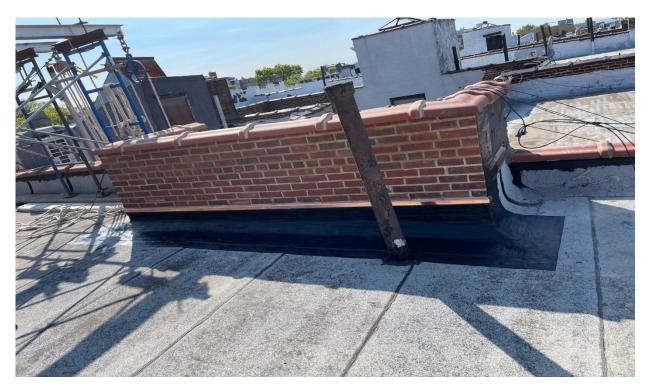



Office 718-369-1001 Fax 718-369-7059

Additional dust control installed






Office 718-369-1001 Fax 718-369-7059

Cutting is done 100%. All pointing will be done 100% 5/15/23





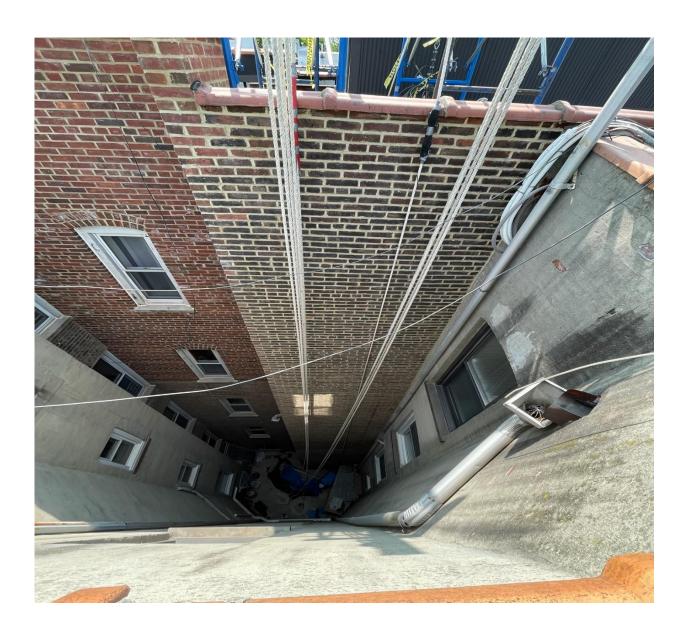









Office 718-369-1001 Fax 718-369-7059



All contracted masonry and parapet wall is completed

5/15/23 **Douglas Gornick**
